

DEC 23 2019

Option #1

REQUEST FOR AGENDA PLACEMENT FORM**Approved**

Submission Deadline - Tuesday, 12:00 PM before Court Dates

SUBMITTED BY: Rexann Knowles

TODAY'S DATE: 12/16/19

DEPARTMENT:

COUNTY JUDGE

SIGNATURE OF DEPARTMENT HEAD:

X _____

REQUESTED AGENDA DATE:

December 23, 2019

SPECIFIC AGENDA WORDING: Consideration of Environmental Review Record, Environmental Assessment and Authority to Use Grant Funds, Johnson County TX CDBG Contract No. 7218250 Water Improvements for Environmental Clearance for the Reduced Scope of Work (Option 1, Option 2)

PERSON(S) TO PRESENT ITEM: Rexann KnowlesSUPPORT MATERIAL: (Must enclose supporting documentation)

TIME: 2 minutes

ACTION ITEM: X

WORKSHOP: _____

(Anticipated number of minutes needed to discuss item) CONSENT: _____

EXECUTIVE: _____

STAFF NOTICE:

COUNTY ATTORNEY: XX

IT DEPARTMENT: _____

AUDITOR: XX

PURCHASING DEPARTMENT: _____

PERSONNEL: _____

PUBLIC WORKS: _____

BUDGET COORDINATOR: _____


OTHER: _____

*****This Section to be Completed by County Judge's Office*****

ASSIGNED AGENDA DATE: _____

REQUEST RECEIVED BY COUNTY JUDGE'S OFFICE _____

COURT MEMBER APPROVAL _____ Date _____



12/17/19

2201 Northland Drive
Austin, Texas 78756
Office: (512) 420-0303
Fax: (512) 420-0302

RE: CD- 7218250

Dear Johnson County Commissioners court

Please use the supporting documents in this packet for your agenda on Dec 23, 2019, which includes maps for Option 1 and Option 2. Option 1 has the reduced scope of work and stops at the archeological buffer point. Option 2 has the original scope of work, but skips the archeological site and continues past it.

I highly recommend continuing the work that is displayed in Option 1.

After speaking with Eddy, from the engineer contact and Dana, from JSUD, they both agree that Option 1 would be a better outcome.

Thank you,

Missy Carugati

PM Community Development
Grantworks

Johnson County CDBG- 7218250

Option 1- reduced scope = 3,975 LF

Pros:

1. we have the area environmentally cleared and the AUGF
2. we can move forward with starting the bid process for construction.
3. save money and time

Cons:

1. the scope of work is reduced

Option 2 = 3,975 +1,625 LF

Pros:

1. more water line

Cons:

1. more than likely need to apply for extension, may not get approved
2. environmental re-evaluation, more time- 1-2 months
3. archeologist will need to be onsite during construction \$\$\$\$\$
4. THC will need to review area and let us know where exactly which point we could start construction, if we even can. more time, possibly 1-3 months
5. we will need a performance statement modification

OPTION 1




2017 TXCDBG PROGRAM
FOR
JOHNSON COUNTY SPECIAL UTILITY DISTRICT
JOHNSON COUNTY, TEXAS



Daniel & Brown Inc.
118 McKinney St.
P.O. Box 606
Farmersville, Texas 75442
Phone 972-784-7777
www.DBIConsultants.com
Firm Registration No.: F-002225

OPTION 2

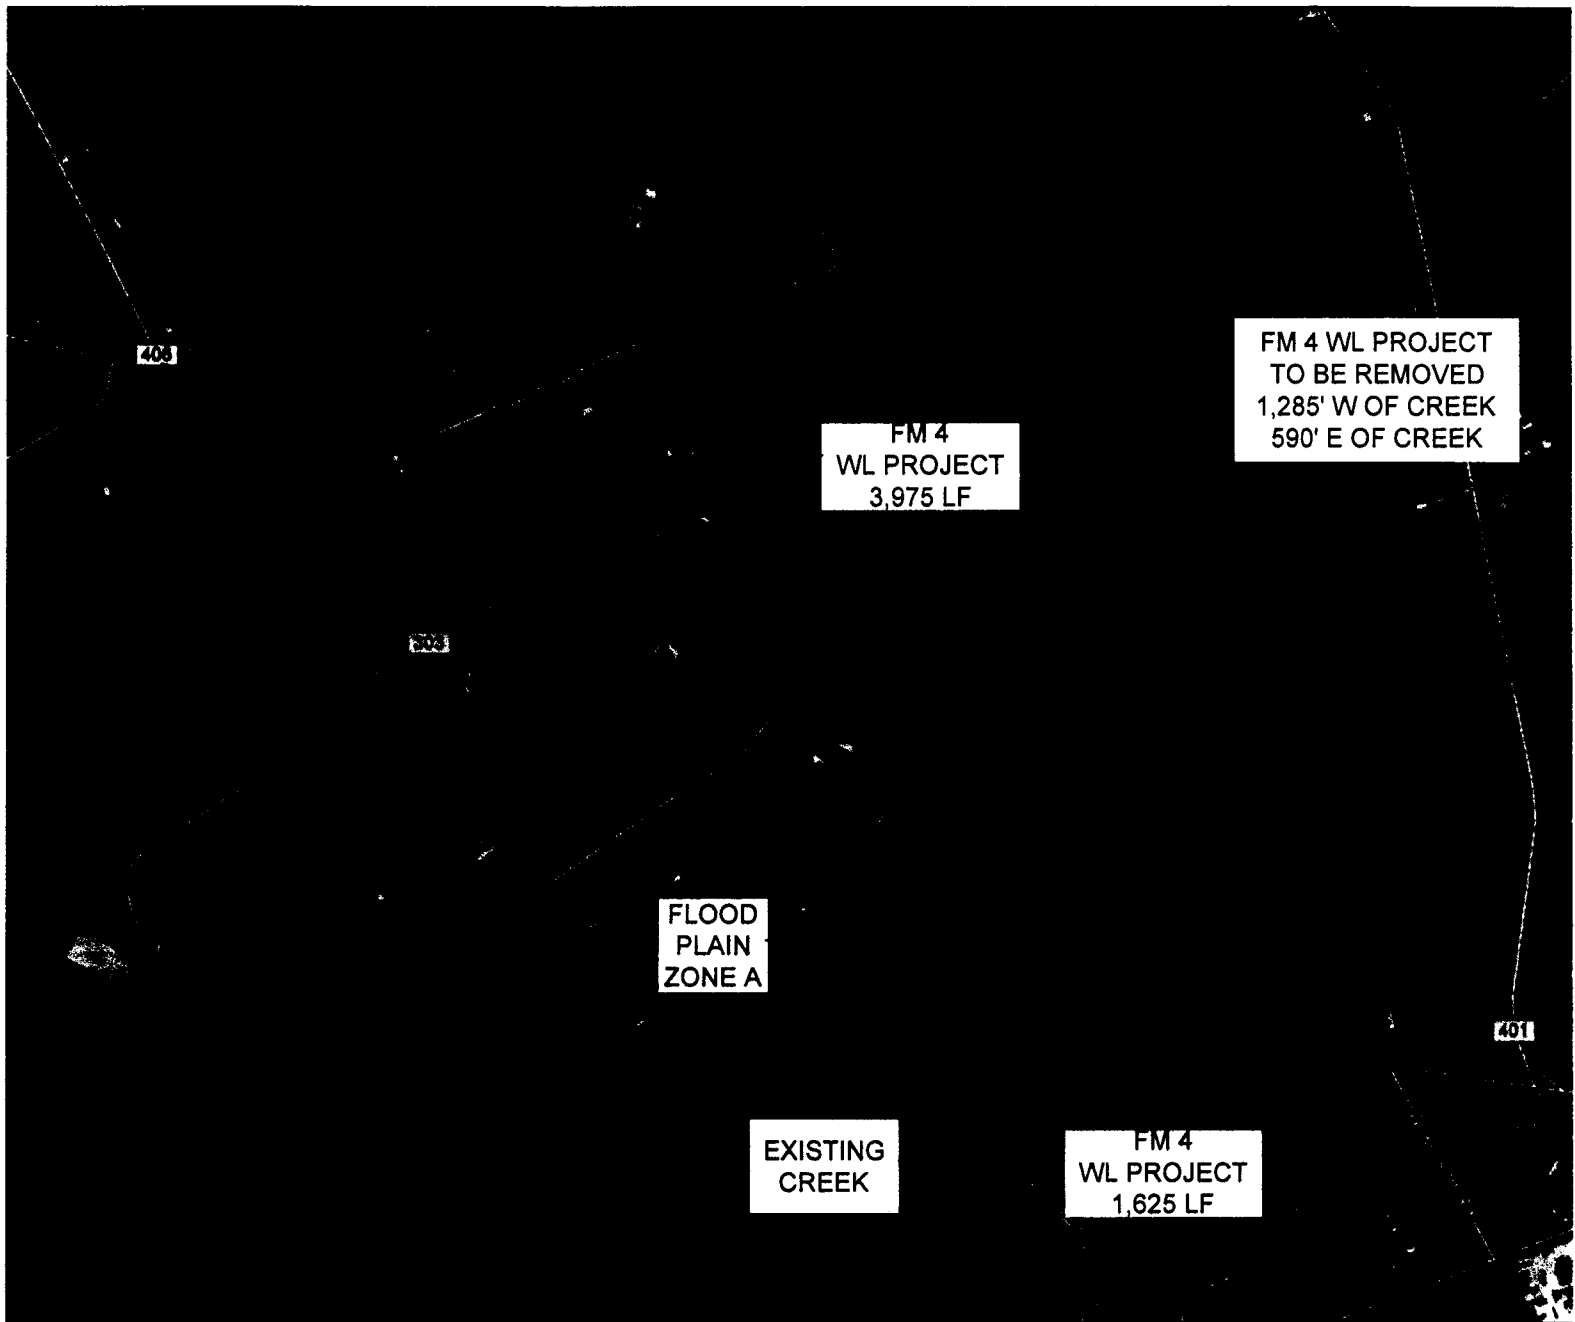

REVISED SITE PLAN - 12-09-2019

2017 TXCDBG PROGRAM
FOR
JOHNSON COUNTY SPECIAL UTILITY DISTRICT
JOHNSON COUNTY, TEXAS



Daniel & Brown Inc.
118 McKinney St.
P.O. Box 606
Farmersville, Texas 75442
Phone 972-784-7777
www.DBIConsultants.com
Firm Registration No.: F-002225

Dana Collier

11:09 AM (1
hour ago)

to Terry, Barbara, countyjudge, eddy, aaron, me, Rexann

Missy-

Due to the amount of time it takes to get clearance through THC and Environmental, JCSUD will go with OPTION 1 on the HWY 4 project.

With the Environmental clearance, what do we (JCSUD) need to get to you to get started on the easement acquisition for the 3 properties?

Dana Collier

System Development Manager
Johnson County Special Utility District
(817) 760-5226
dcollier@icsud.com
